
Glashaboy Flood Relief Scheme

Programme Update September 2016

Cork County Council

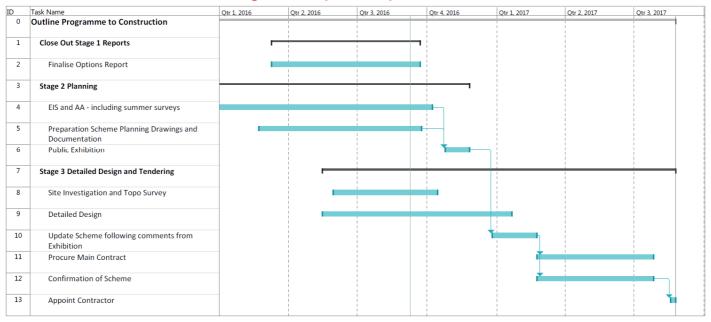

Progress Update Summary

Stage 1	Stage 2	Stage 3				
Reports	Planning	Detailed Design and Tendering				
Activities this Period Sep 2016						
Close out remaining draft stage 1 Options Report	Complete Arborist Survey. Stakeholder consultation	Topographical and CCTV Survey nearing completion. Site Investigation nearing completion				
	Complete EIS	Progress Scheme Detailed Design.				
Activities next period Sep – Oct 2016						
	Continue Scheme Planning Drawings and EIS	Continue Scheme Datailed Design				
	Public Exhibition	Continue Scheme Detailed Design.				
Key Drivers and Constraints						
	Arborist survey	Tender Process – EU procurement rules				
	Statutory Requirements of Arterial Drainage Acts	Tender Process – Eo procurement rules				
Key Risks						
	Arborist survey – further work required	Amendments to scheme design following Public Exhibition				
	Landowner disputes	Funding				
	Marginal Benefit Cost Ratio of Scheme	Tender process - legal challenges unsuccessful tenderers				

Scheme Details

Copper Valley Vue – Glenmore Stream – flood relief culvert – conveyance improvements St Patrick's Mill and The Fountains- individual property protection measures The Groves: Glashaboy River – direct flood defences Glanmire Business Park to Barry's Terrace – Glashaboy River - 635m flood defence wall	Works Scope:	St Patrick's Mill and The Fountains- individual property protection measures The Groves: Glashaboy River – direct flood defences	Cost	Construction estimated cost €7.1m incl. VAT Consultants - Arup €525,000 incl. VAT (estimated based on construction cost estimate) Funding : 100% OPW
--	--------------	---	------	--

